

# Works Completed during the last week.

**Week 120: Monday 10 March to Friday 14 March 2008**

- With the planned opening of the new defences only weeks away, works on site have concentrated on installing the finishing touches to the scheme, including installation of fencing, handrailing, and litter bins.
- To the north of the site work has continued on the installation of the roadside conservation kerbing and infilling behind with stone in preparation for the construction of the new exposed aggregate concrete pavement.
- Adjacent to the new café building the timber templates have been removed from the interactive shower feature in preparation for the infilling with blue glass resin.



Preparation of the new water feature ahead of the application of the blue glass resin




Construction of the roadside kerbing and pavement under construction

- At the southern end of the site, works have concentrated on installing the furniture to complete the Plaza Area. Works have included
  - Installation of pedestrian handrailing to steps and access slopes
  - Installation of stainless steel studs to mark steps and changes in promenade profile
  - Installation of litter bins and cycle racks



Installing stainless steel studs to indicate the top of a set of steps

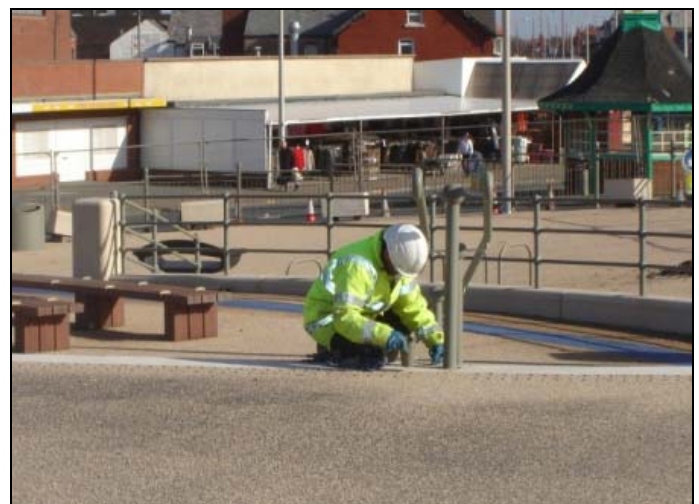

Installing handrailing within the Plaza area

Further information about the scheme can be viewed at  
[www.wyrebc.gov.uk](http://www.wyrebc.gov.uk)  
[www.cleveleys-seawall.co.uk](http://www.cleveleys-seawall.co.uk)

**Birse**  
**Coastal**  
A Balfour Beatty Company

working in partnership with  
**Wyre Borough Council**  
LIVE WYRE LOVE WYRE
