

Works Completed during the last week.

Week 130: Monday 19 May to Friday 23 May 2008

- Piling work on Phase 4 of the Cleveleys sea defence and promenade improvement works was completed this week.
- Work began on the import and placement of 3000 tonne of rock armour this week. These 4 tonne pieces of rock will be placed on the beach along the pile line and will be used temporarily to protect the the ground stabilisation works due to commence next week. Following completion of the revetment this rock will then be used as part the new groynes.



Loading rock armour prior to placement on the beach.




Rock armour in place on the beach.

- Installation of the water feature equipment continued this week.
- United Utilities continued installation of the electric supply to the cafe.
- The final touches to the landscaping between Carr Gate and Victoria Road was completed.



Installation of pipework within water feature.

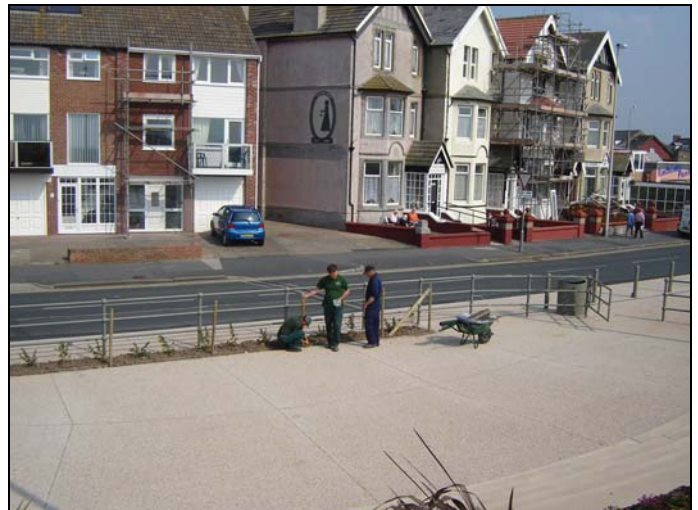

Landscaping works.

Further information about the scheme can be viewed at
www.wyrebc.gov.uk
www.cleveleys-seawall.co.uk

Birse
Coastal
A Balfour Beatty Company

working in partnership with
Wyre Borough Council
LIVE WYRE LOVE WYRE
