

Works Completed during the last week.

Week 137: Monday 7 July to Friday 11 July 2008

- Work on the ground stabilisation element of the project was completed this week. A total of 683 vibro stone columns have been installed between Victoria Road and Kingsway to strengthen the poor ground conditions. This work will significantly improve the load bearing capacity of the ground, allowing the permanent works to be constructed on a sound foundation
- A layer of stone 'rip rap' has been placed as protection to the piles until the permanent works can be put in place. The permanent works are due to commence in October 2008.




The piling rig placing the last of the stone columns.



Final rip rap protection to the stone columns.

- Commissioning of all the various electrical and mechanical elements of the cafe building continued this week. Work completed includes the general electric and plumbing of the building, fire alarm, roller shutter doors and outdoor shower.
- Works yet to complete include the public toilets, the water play area, intruder alarm, CCTV system and automatic sliding doors.
- It is anticipated that the new Danfo toilets will be opened to the public during the coming week.

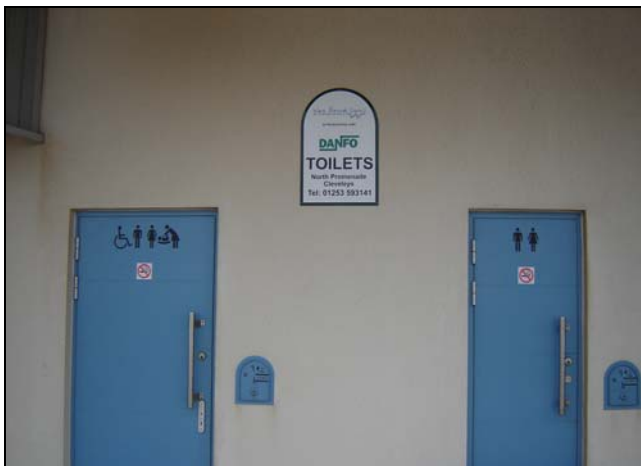

Public toilets at The New Wave.



The New Wave building.

Further information about the scheme can be viewed at
www.wyrebc.gov.uk
www.cleveleys-seawall.co.uk

Birse
Coastal
A Balfour Beatty Company

working in partnership with
Wyre Borough Council
LIVE WYRE LOVE WYRE
